

San Marcos Consolidated Independent School District

Construction Update Hernandez Elementary School – Re-Roof




San Marcos CISD Board Meeting
September 17, 2018

Hernandez Elementary School Re-Roof

Activity Briefing

Completed Activity:

- Completed installation of roof huggers and insulation on building D.
- Began demolition of existing r-panel fascia and soffits on building D and installation of new soffits, fascia, and gutter.
- Completed installation of gutter on Canopies K, J, and H
- Completed installation of panels on Canopies K and J
- Installed roof huggers and insulation on Corridors G-1 through G-4.
- Began installation of wood nailers on building E.
- Began installation of roof huggers and insulation on building B.

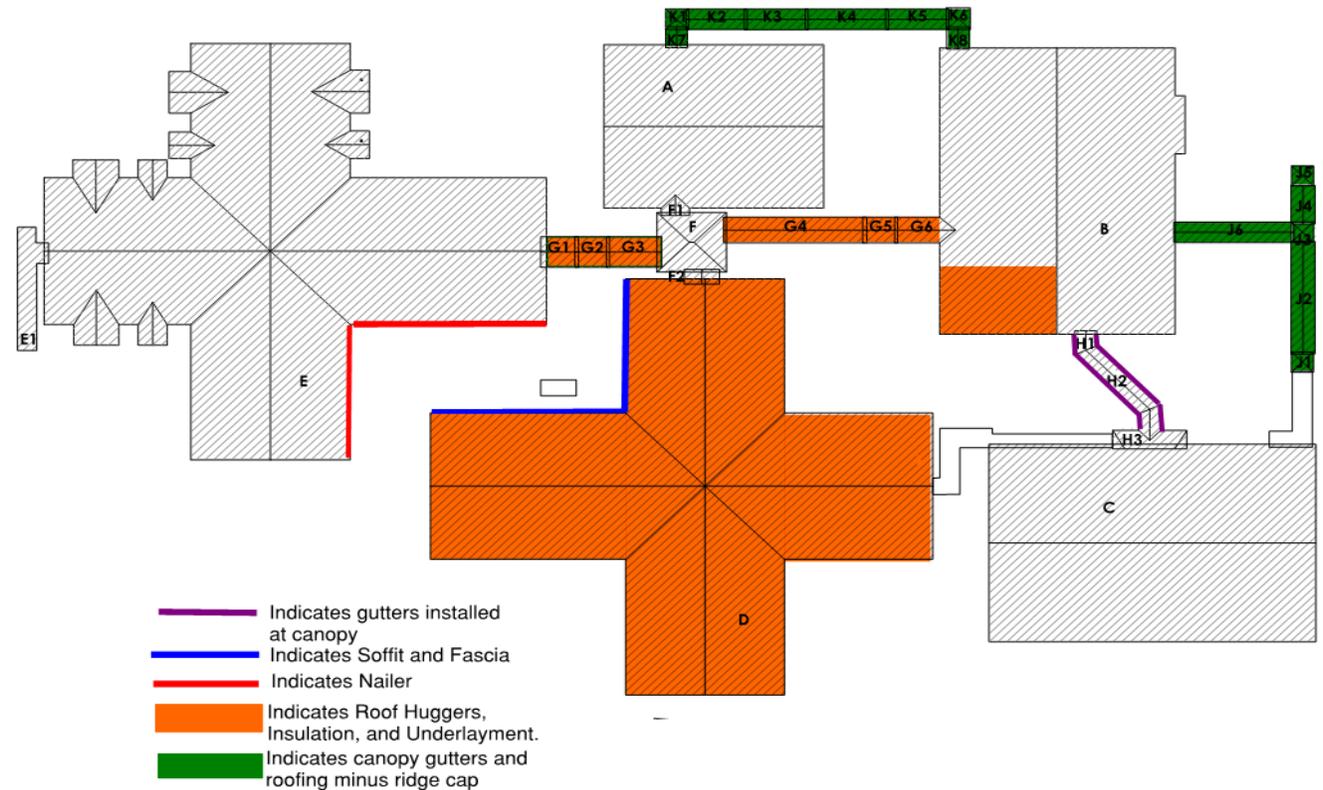

Hernandez Elementary School Re-Roof



Description: Completed installation of roof hugger system and insulation panels with rain/ice shield installed on Building D

Hernandez Elementary School Re-Roof



Description: Installation of new soffits and fascia on Building D

Hernandez Elementary School Re-Roof



Description: Installation of Roof Hugger System and Insulation on Building B (Cafeteria)

Hernandez Elementary School Re-Roof



Description: Installation of Roof Hugger System and Insulation on Corridors G5 and G6

Hernandez Elementary School Re-Roof



Description: Installation of Wood Nailer on Building E

Hernandez Elementary School Re-Roof

Work Tasks Prior to 10/11/18:

- Installation of gutters and panels on Canopy E1
- Installation of panels on Canopy H
- Installation of Roof Huggers and Insulation on Building B
- Installation of panels on Building D
- Installation of R-panel fascia and soffits on Building D
- Continued installation of wood nailers on Building E
- Begin installation of Roof Huggers and insulation on Building E
- Begin demolition of soffits and fascia on Building B and Building E

Hernandez Elementary School Re-Roof

